



New Westminster Interceptor

COLUMBIA STREET SECTION REHABILITATION – PROJECT UPDATE

Colin Meldrum, P. Eng.

Director, Engineering, Design & Construction

City of New Westminster Council Meeting

March 7, 2022

ON TABLE

City Council Meeting

March 7, 2022


re: Item 3.1

metrovancouver

INTRODUCTION

- Overview
- Schedule
- Progress
- Next steps

OVERVIEW

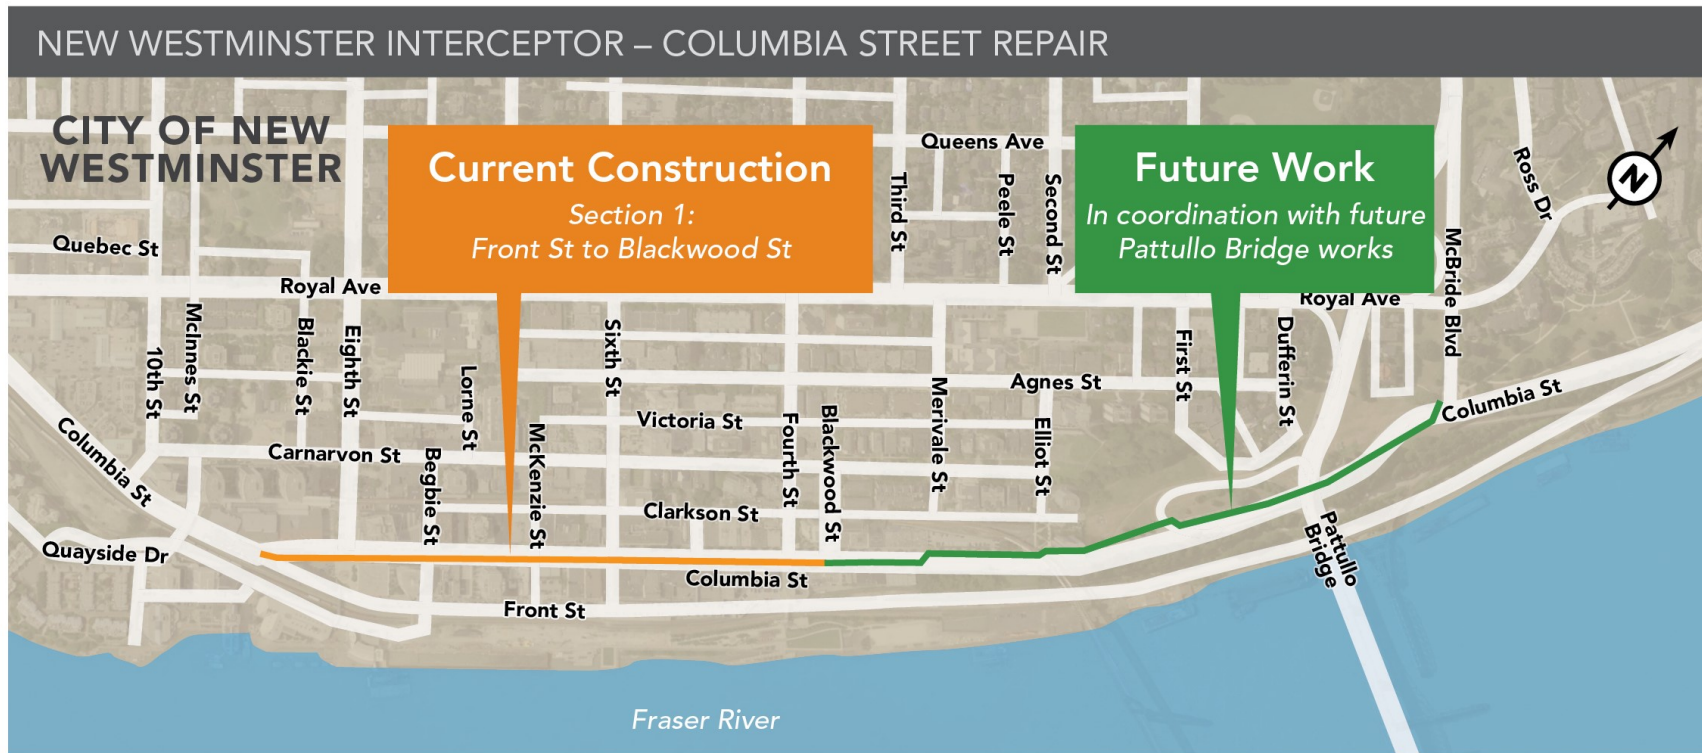

SCHEDULE

2021

2022

MAY

JUN

JUL

AUG

SEP

OCT

NOV

DEC

JAN

FEB

MAR

APR

MAY

Original timeline
(March 2021)

4 – 5 months

Revised timeline
(June 2021)

~6 months (summer 2021 to early 2022)

Current timeline
(February 2022)

onboarding

pipe
delivery

weather

omicron

Water main work

PHASE 1 PROGRESS

- Slip-lining: 30% complete, remaining completed in 3 weeks
- Remaining work: manhole installations, connections, manhole removals, restoration

NEXT STEPS

- Upcoming patio season and summer events
- Focus on getting the work done
- Continue weekly updates to the community



Questions?

metrovancouver
Together we make our region strong

PROJECT OVERVIEW



PROJECT OVERVIEW

